parakeet communities

INTERNAL BUILD SPECIFICATION

WORKFLOW #002

Rehab

Quickbase + FastField Build Specification
Existing Home Rehabilitation — Vacant to Ready to Market

Parakeet Communities · Internal · Confidential

VERSION	DATE	WORKFLOW ID
v1.0	08/18/26	WF002

DRAFT FOR REVIEW

Scope: This document specifies the Quickbase tables, workflow stages, automations, gate rules, and FastField form for Workflow #002: Rehab. Applies to existing homes in the portfolio requiring rehabilitation before re-listing or re-occupancy. Companion document to WF001 — Home Ordering, Delivery & Set.

Table of Contents

1. Document Purpose 2
2. Workflow Overview 2
3. Workflow Stages 3
4. Quickbase Tables 4
4.1 Rehab Records (RH) 4
4.2 Rehab Tasks (TK-RH) 5
4.3 Rehab Walkthrough Records (RW) 5
5. FastField Form – Rehab Walkthrough Punchlist 8
6. Cascading Dropdown Architecture (WF002) 9
7. Automations 9
8. Gate Rules 10
9. Open Items 11
10. Spec Version History 12

SECTION 01 Document Purpose

WF002 – Rehab

This specification defines the complete Quickbase (QB) tables, workflow stages, automations, gate rules, and FastField form required to build Workflow #002: Rehab. This workflow manages the end-to-end process of taking a vacant home from initial identification of rehab need through completed rehab, final walkthrough approval, and handoff to the listing workflow.

Workflow #002 is independent of Workflow #001 (Home Ordering). It applies to *existing homes* in the portfolio – homes that have been vacated via move-out or otherwise identified as needing rehab before they can be re-listed or re-occupied. WF001 covers new homes ordered from manufacturers; WF002 covers existing portfolio assets.

> **System of Record:** Rent Manager (RM) remains the system of record for asset data, financial records, and insurance. This build complements RM – it does not replace or auto-modify any RM records. All Rent Manager field references in QB are cross-references only.

BOUNDARY	DETAIL
In Scope	All 9 rehab workflow stages; QB Rehab Records, Rehab Tasks, and Walkthrough Records tables; FastField Rehab Walkthrough Punchlist form; FastField → QB webhook integration; all automations and gate rules defined in this document
Out of Scope	Rent Manager asset record creation or modification; marketing execution post-listing; Workflow #001 (new home ordering); financial/invoice processing; vendor portal or external work order systems
Dependent Workflows	WF001 Stage 9 (Listing) – WF002's final stage hands off to the listing process. Move Out workflow – completed move-out can auto-trigger a WF002 record.

SECTION 02 Workflow Overview

WF002 – Rehab

WORKFLOW ID	WORKFLOW NAME	STATUS
WF002	Rehab	DRAFT FOR REVIEW

APPLIES TO	PRIMARY ACTOR	SYSTEM OF RECORD
Existing homes – vacant, requiring rehab	Community Manager + Ops Team	Rent Manager

TRIGGER

Move Out completion (auto) OR Manual creation	OUTCOME Rehab Approved → Ready to Market	STAGES 9 (incl. 1 conditional loop)

Relationship to Other Workflows


RELATED WORKFLOW	RELATIONSHIP
WF001 – Home Ordering	Separate workflow for new homes from manufacturers. WF002 covers existing portfolio homes only. No overlap; WF002 connects at WF001 Stage 9 (Listing) only at handoff.
Move Out (separate QB table)	A completed Move Out record can auto-trigger creation of a WF002 Rehab Record for the same lot/asset (Automation A-RH-01).
Listing Workflow	WF002 Stage 9 (Handed to Listing) triggers the listing process. A "Rehab Approved" home feeds directly into listing. Automation A-RH-08 handles the handoff.

Trigger Clarification (Open Item O-WF002-01): Confirm whether WF002 can also be triggered manually – e.g., for acquired homes, homes with existing damage, or portfolio-wide rehab reviews – independent of a move-out event. Manual trigger option should be supported unless confirmed otherwise.

SECTION 03 Workflow Stages

9 Stages – 1 Conditional Loop

Nine stages define the full lifecycle from vacancy identification through market-ready handoff. Stage 7 is a **conditional loop** – entered only when the walkthrough does not pass. A passing walkthrough advances directly from Stage 6 → Stage 8, skipping Stage 7.

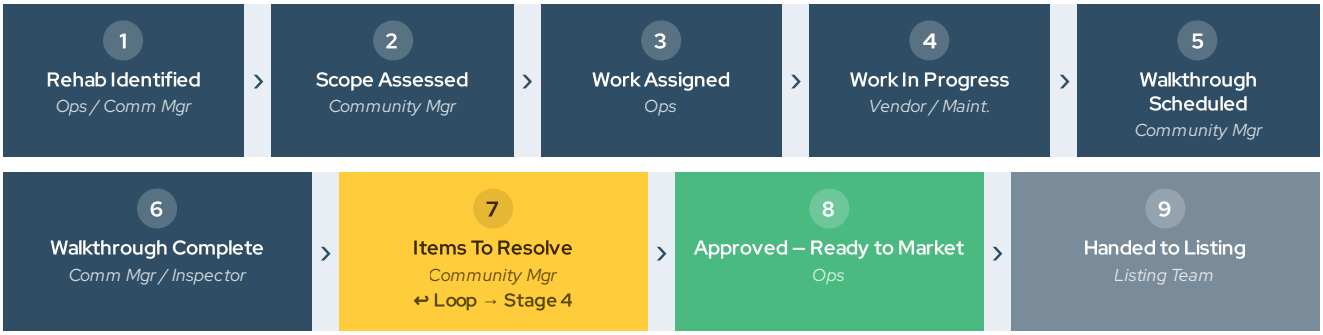

Stage 7 (amber): Conditional loop – entered only when Walkthrough Status = Needs Additional Items, Not Ready, or Vendor Needs to Finish. Loops back to Stage 4. Skipped entirely on first-pass approval (Stage 6 → Stage 8 direct).

Table 3-1 Stage Detail Reference

#	STAGE NAME	OWNER	DESCRIPTION
1	Rehab Identified	Ops / Community Mgr	Home flagged for rehab. Record created in QB. Asset status updated to In Rehab. Rehab ID auto-generated.
2	Scope Assessed	Community Mgr	Physical assessment complete. Scope of work documented in QB Scope Notes field. Gate: Scope Notes must not be blank before advancing.
3	Work Assigned	Ops	Vendor or maintenance staff assigned. Work orders (Rehab Tasks records) created in QB. Gate: Assigned To field must be populated.
4	Work In Progress	Vendor / Maintenance	Active rehab underway. QB Rehab Tasks updated as items are completed. Gate: at least one Task must exist with status = In Progress or Complete.

5	Walkthrough Scheduled	Community Mgr	Final walkthrough date set. QB automation generates the pre-populated FastField launch link. Gate: Walkthrough Scheduled Date must be set.
6	Walkthrough Complete	Community Mgr / Inspector	FastField Rehab Walkthrough Punchlist submitted. Webhook creates child Walkthrough Record. Results parsed. Walkthrough Status set. Gate: at least one Walkthrough Record must exist.
7	Items To Resolve	Community Mgr	*Conditional – triggered only when Walkthrough Status ≠ Approved.* Follow-up tasks created in Rehab Tasks. Loops back to Stage 4 when tasks are complete and re-inspection scheduled.
8	Approved – Ready to Market	Ops	Walkthrough Status = Approved as Ready to Market. Asset Status updated to Available. Approved Date set. Listing team notified.
9	Handed to Listing	Listing Team	Listing workflow triggered (Automation A-RH-08). Rehab Record closed. Asset proceeds to listing process.

SECTION 04 Quickbase Tables

3 Tables – Primary + 2 Child Tables

4.1 Rehab Records (RH) – Primary Table

One record per home rehab project. Parent to Rehab Tasks and Walkthrough Records. Record ID format: RH-YYYY-### (e.g., RH-2026-001).

Table 4-1 Rehab Records – Field Definitions

FIELD NAME	FIELD TYPE	NOTES / RULES
Rehab ID	*Text (auto-generated)*	Format: RH-YYYY-###. Set by Automation A-RH-02 on record creation.
Community	Relationship → Communities	Required. Cascading – top of the Community → Lot → Asset chain.
Lot	Relationship → Lots	Required. Filtered to selected Community. Lot Status must be In Rehab or Available.
Asset	Relationship → Assets	Required. Filtered to selected Lot. Asset Status must be In Rehab.
RM Asset Record #	Text	Cross-reference to Rent Manager asset record. Manual entry only – do not auto-sync.
RM Unit #	Text	Cross-reference to Rent Manager unit number. Manual entry only – do not auto-sync.
Rehab Stage	Dropdown	Values: Rehab Identified / Scope Assessed / Work Assigned / Work In Progress / Walkthrough Scheduled / Walkthrough Complete / Items To Resolve / Approved – Ready to Market / Handed to Listing.
Triggered By	Dropdown	Values: Move Out / Manual / Acquisition. Determines source of rehab identification.
Source Move Out Record #	Relationship → Move Out Records	Populated only if Triggered By = Move Out. Links Rehab Record to the originating Move Out event.
Rehab Identified Date	Date	mm/dd/yy. Auto-populated when record is created.
Scope Assessed Date	Date	mm/dd/yy. Set when Stage advances to Scope Assessed.
Work Assigned Date	Date	mm/dd/yy. Set by Automation A-RH-03.
Work In Progress Date	Date	mm/dd/yy. Set when Stage advances to Work In Progress.
Walkthrough Scheduled Date	Date	mm/dd/yy. Set by Automation A-RH-04. Gate field for Stage 5.

Walkthrough Completed Date	Date	mm/dd/yy. Set by Automation A-RH-05 on FastField submission.
Approved Date	Date	mm/dd/yy. Set by Automation A-RH-06 when Walkthrough Status = Approved.
Assigned To	Text	Vendor name or staff member. Gate field – must not be blank before Stage 3 → Stage 4 transition.
Scope Notes	Text (multi-line)	Description of full rehab scope. Gate field – must not be blank before Stage 2 → Stage 3 transition.
Walkthrough Status	Dropdown	Values: Approved as Ready to Market / Needs Additional Items / Not Ready / Vendor Needs to Finish. Drives Stage 7 vs. Stage 8 routing (see Gate G-RH-06).
Days In Rehab	*Duration (calculated)*	Rehab Identified Date → Approved Date. Drives overdue alerts (A-RH-10 at 30 days; A-RH-11 at 60 days).
FastField Launch Link	URL	Pre-populated link to FastField Rehab Walkthrough Punchlist. Auto-generated by Automation A-RH-04. Includes Community, Lot, Asset, and Rehab Record ID as URL parameters.
Record Created By	*Text (auto)*	QB user who created the record. Auto-populated.
Last Updated	*Date/Time (auto)*	QB auto-stamp on every save.

4.2 Rehab Tasks (TK-RH) – Child Table

One record per work item or assignment. Child of Rehab Records. Multiple tasks per Rehab Record. Record ID format: TK-RH-YYYY-##### (e.g., TK-RH-2026-00001).

Table 4-2 Rehab Tasks – Field Definitions

FIELD NAME	FIELD TYPE	NOTES / RULES
Task ID	*Text (auto-generated)*	Format: TK-RH-YYYY-#####. Auto on record creation.
Parent Rehab Record	Relationship → Rehab Records	Required. Links task to its parent rehab project.
Task Name	Text	Required. Free-text description of the specific work item.
Category	Dropdown	Values: Interior / Doors & Hardware / Kitchen / Bathrooms / Utilities / Exterior / Other.
Assigned To	Text	Vendor name or staff member handling this specific task.
Assigned Date	Date	mm/dd/yy. Date task was assigned to vendor/staff.
Due Date	Date	mm/dd/yy. Expected completion date. Used in overdue reporting.
Status	Dropdown	Values: Not Started / In Progress / Complete / Blocked. Gate field – all tasks must be Complete before Stage G-RH-07 allows walkthrough re-scheduling.
Completion Date	Date	mm/dd/yy. Set when Status changes to Complete.
Notes	Text (multi-line)	Additional context, blockers, or completion notes.

4.3 Rehab Walkthrough Records (RW) – Child Table

One record per FastField walkthrough submission. Child of Rehab Records. Multiple submissions possible (one per walkthrough attempt). Populated via webhook from FastField. Record ID format: RW-YYYY-### (e.g., RW-2026-001).

Table 4-3 Rehab Walkthrough Records – Field Definitions

FIELD NAME	FIELD TYPE	NOTES / RULES

HEADER FIELDS		
Walkthrough Record ID	*Text (auto)*	Format: RW-YYYY-###. Auto on record creation from webhook.
Parent Rehab Record	Relationship → Rehab Records	Required. Matched by Rehab Record ID from FastField payload.
FastField Submission ID	Text	UUID from FastField webhook payload. Stored for audit traceability.
Community	Relationship → Communities	From FastField (pre-populated on form open). Cross-checks parent record.
Lot	Relationship → Lots	From FastField (pre-populated). Cross-checks parent record.
Submitted By	Text	Manager name as entered on the FastField form.
Manager Email	Email	From FastField form field. Used for notification routing.
Walkthrough Date	Date	mm/dd/yy. Date of walkthrough as entered on the form.
SECTION A – INTERIOR (10 ITEMS)		
Home Smells Clean	Checkbox (Yes / No)	Interior condition indicator.
No Trash / Debris	Checkbox (Yes / No)	
Floors Swept / Mopped / Vacuumed	Checkbox (Yes / No)	
Cabinets / Counters / Appliances Cleaned	Checkbox (Yes / No)	
Blinds Installed / Clean / Working	Checkbox (Yes / No)	
Outlet / Switch Covers Installed	Checkbox (Yes / No)	
Interior Bulbs Working	Checkbox (Yes / No)	
Smoke Detectors Working	Checkbox (Yes / No)	
Bath / Toilets / Sinks Cleaned	Checkbox (Yes / No)	
Windows Cleaned	Checkbox (Yes / No)	
SECTION B – DOORS, HARDWARE & SAFETY (5 ITEMS)		
Front Door Handle / Lock Good or Replaced	Checkbox (Yes / No)	
Deadbolt Works / Keys Labeled	Checkbox (Yes / No)	
Interior / Closet Doors Work	Checkbox (Yes / No)	
Windows Open / Close / Lock	Checkbox (Yes / No)	
Steps / Porch / Handrails Safe	Checkbox (Yes / No)	
SECTION C – KITCHEN & APPLIANCES (6 ITEMS)		
Refrigerator Clean / Working	Checkbox (Yes / No)	
Stove / Oven Clean / Working	Checkbox (Yes / No)	
Dishwasher / Range Hood Works	Checkbox (Yes / No)	
Sink / Faucet Works	Checkbox (Yes / No)	
No Leaks Under Sink	Checkbox (Yes / No)	
Cabinets / Drawers Work	Checkbox (Yes / No)	

SECTION D – BATHROOMS & PLUMBING (6 ITEMS)		
New Toilet Seat Installed	Checkbox (Yes / No)	
Toilet Flushes	Checkbox (Yes / No)	
Sink / Shower / Tub Work	Checkbox (Yes / No)	
No Leaks	Checkbox (Yes / No)	
Mirror / Vanity / Towel Bar Secure	Checkbox (Yes / No)	
Caulking Clean / Complete	Checkbox (Yes / No)	
SECTION E – UTILITIES & VACANT HOME CHECK (5 ITEMS)		
Electric On / Staying On	Checkbox (Yes / No)	
Water On / Staying On	Checkbox (Yes / No)	
Heat / A/C Works	Checkbox (Yes / No)	
Toilets Flushed / Water Run in Sinks	Checkbox (Yes / No)	
Checked for Leaks / Odors / Pests / Vandalism	Checkbox (Yes / No)	
SECTION F – EXTERIOR & LANDSCAPING (5 ITEMS)		
Exterior Clean / Power Washed	Checkbox (Yes / No)	
Skirting Secure / Presentable	Checkbox (Yes / No)	
Yard Cleaned / Grass Cut / Weeds Handled	Checkbox (Yes / No)	
Landscaping Complete or Assigned	Checkbox (Yes / No)	
Landscaping Owner	Dropdown	Values: Maintenance / Manager / Vendor. Required when Landscaping Complete or Assigned = Yes.
SECTION G – POST-WALKTHROUGH STATUS & CALCULATED FIELDS		
Walkthrough Status	Dropdown	Values: Approved as Ready to Market / Needs Additional Items / Not Ready / Vendor Needs to Finish. Drives routing automation (A-RH-06 or A-RH-07).
Inspector Signature	Signature	Captured in FastField. Stored as image attachment in QB record.
Items Passed	*Number (calculated)*	Count of Yes responses across all 37 checklist items.
Items Failed	*Number (calculated)*	Count of No responses across all 37 checklist items.
Pass Rate	*Percentage (calculated)*	Items Passed ÷ 37 × 100. Display format: xx.x%. Example: 35 of 37 = 94.6%.

SECTION 05 FastField Form – Rehab Walkthrough Punchlist

37 Checklist Items · 8 Sections

FORM NAME	FORM TYPE	LAUNCH METHOD
PARAKEET – WF002 – Rehab Walkthrough Punchlist	Field inspection / punchlist	Pre-populated link from QB Rehab Record

INTEGRATION	MATCHING KEY	TOTAL ITEMS
Webhook JSON POST → QB Rehab Walkthrough Records	Rehab Record ID (pre-populated, locked)	37 checklist items (36 Yes/No + 1 dropdown)

Launch Flow: Field crew navigates to the Rehab Record in QB. QB displays a pre-populated FastField launch link (generated by Automation A-RH-04). Tapping the link opens FastField with Community, Lot, Asset, and Rehab Record ID already filled in and locked. Manager adds their name, email, and walkthrough date, then completes the 37 checklist items. On submission, the webhook creates a child Walkthrough Record in QB instantly.

Table 5-1 FastField Form Structure

#	SECTION NAME	ITEMS	FIELDS / DETAILS
1	Header	6 fields	**Community** (pre-populated, locked) · **Lot / Unit** (pre-populated, locked) · **Rehab Record ID** (pre-populated, locked – matching key) · **Manager Name** (text, required) · **Manager Email** (email, required) · **Date of Walkthrough** (date, default = today)
2	Interior	10 Yes/No	Home Smells Clean · No Trash/Debris · Floors Swept/Mopped/Vacuumed · Cabinets/Counters/Appliances Cleaned · Blinds Installed/Clean/Working · Outlet/Switch Covers Installed · Interior Bulbs Working · Smoke Detectors Working · Bath/Toilets/Sinks Cleaned · Windows Cleaned
3	Doors, Hardware & Safety	5 Yes/No	Front Door Handle/Lock Good or Replaced · Deadbolt Works/Keys Labeled · Interior/Closet Doors Work · Windows Open/Close/Lock · Steps/Porch/Handrails Safe
4	Kitchen & Appliances	6 Yes/No	Refrigerator Clean/Working · Stove/Oven Clean/Working · Dishwasher/Range Hood Works · Sink/Faucet Works · No Leaks Under Sink · Cabinets/Drawers Work
5	Bathrooms & Plumbing	6 Yes/No	New Toilet Seat Installed · Toilet Flushes · Sink/Shower/Tub Work · No Leaks · Mirror/Vanity/Towel Bar Secure · Caulking Clean/Complete
6	Utilities & Vacant Home Check	5 Yes/No	Electric On/Staying On · Water On/Staying On · Heat/A/C Works · Toilets Flushed/Water Run in Sinks · Checked for Leaks/Odors/Pests/Vandalism
7	Exterior & Landscaping	5 items	Exterior Clean/Power Washed (Y/N) · Skirting Secure/Presentable (Y/N) · Yard Cleaned/Grass Cut/Weeds Handled (Y/N) · Landscaping Complete or Assigned (Y/N) · Landscaping Owner (dropdown: Maintenance / Manager / Vendor)
8	Post-Walkthrough Status	2 fields	**Walkthrough Status** (dropdown, required): Approved as Ready to Market / Needs Additional Items / Not Ready / Vendor Needs to Finish · **Manager/Inspector Signature** (signature capture, required)

Photo Documentation (Open Item O-WF002-10): The current form spec does not include photo capture fields. Confirm with Austin whether the form should include photos – e.g., one photo per section, or a photo capture triggered by any "No" answer. Photo fields can be added to any section without changing the 37-item count.

SECTION 06 Cascading Dropdown Architecture (WF002)

Community → Lot → Asset

All Community, Lot, and Asset selections in WF002 follow the master cascading chain defined in WF001 Section 3A. The cascade is: **Community → Lot → Asset**. Each selection filters the next dropdown to show only valid child records. WF002 applies the following filters specific to the rehab context.

Table 6-1 WF002 Cascading Dropdown Filter Rules

DROPDOWN	FILTER APPLIED	NOTES
Community	All active communities	No filter – all communities shown. User selects the community where the home is located.
Lot	Lot Status = In Rehab OR Available	Filters to lots in the selected Community that are vacant and eligible for rehab tracking.
Asset	Asset Status = In Rehab	Filters to the specific home on the selected lot that is actively in rehab.

Asset Status Value (Open Item O-WF002-07): "In Rehab" must be added as a valid Asset Status value in the Assets table. Confirm the full set of Asset Status values with Austin before building the Assets table. Recommended values: *In Rehab / Available / Listed / Occupied / Demo / Other*.

FastField Pre-Population: When a field crew member taps the FastField launch link in QB, Community, Lot, Asset, and Rehab Record ID are passed as URL parameters and pre-populated into the form header fields. These four fields are locked (read-only) on the form – the inspector cannot change them. This ensures every submission is correctly matched to its parent QB record.

Lot Status for Rehab (Open Item O-WF002-08): A vacated lot currently carries Lot Status = Available. Confirm whether a separate Lot Status value of "In Rehab" is needed, or whether rehab state is tracked at the Asset Status level only. The current spec tracks rehab state on the Asset (Asset Status = In Rehab) and leaves Lot Status = Available, preserving lot availability metrics while the asset is being rehabbed.

SECTION 07 Automations

11 Automations – QB Pipelines

All automations run in QB Pipelines and fire on record events (field changes, new record creation, or webhook receipt) unless marked Daily. Every automation is numbered with a persistent ID for traceability. Automations are not activated until all Open Items in Section 9 that affect the relevant logic are resolved.

Hard Rule: Automations A-RH-06 and A-RH-07 are mutually exclusive – exactly one fires per walkthrough submission. They are triggered by the value of Walkthrough Status. Both cannot fire on the same record event.

Table 7-1 Automation Register – WF002

ID	TRIGGER	ACTION	TIMING
A-RH-01	Move Out record Status field changed to *Completed*	Auto-create a Rehab Record linked to the same Lot and Asset. Set Rehab Stage = Rehab Identified. Set Triggered By = Move Out. Populate Source Move Out Record # link.	Immediate
A-RH-02	Rehab Record created (Stage = Rehab Identified)	Auto-generate Rehab ID (RH-YYYY-### format). Set Rehab Identified Date = today. Set Asset Status = In Rehab. Notify assigned Ops contact by email.	Immediate
A-RH-03	Rehab Record Stage changed to *Work Assigned*	Set Work Assigned Date = today. Send email notification to the Assigned To contact (vendor or staff) with Rehab ID, Lot, and Scope Notes summary.	Immediate

A-RH-04	Rehab Record Stage changed to *Walkthrough Scheduled*	Generate pre-populated FastField launch link (Community + Lot + Asset + Rehab Record ID as URL parameters). Set Walkthrough Scheduled Date. Notify Community Manager by email with the FastField link.	Immediate
A-RH-05	FastField Rehab Walkthrough Punchlist webhook received	Create child Rehab Walkthrough Record. Map all 37 checklist fields plus header fields. Calculate Items Passed, Items Failed, and Pass Rate. Set Walkthrough Completed Date = today. Update parent Rehab Record: Walkthrough Status = value from form, Stage = Walkthrough Complete.	Immediate
A-RH-06	Walkthrough Status set to *Approved as Ready to Market*	Set Rehab Stage = Approved – Ready to Market. Set Asset Status = Available. Set Approved Date = today. Notify Ops team and Listing team by email.	Immediate
A-RH-07	Walkthrough Status set to *Needs Additional Items* OR *Not Ready* OR *Vendor Needs to Finish*	Set Rehab Stage = Items To Resolve. Create follow-up Rehab Task record with Category = Other and Task Name = "Re-inspect: [Walkthrough Status value]". Notify assigned vendor/maintenance by email.	Immediate
A-RH-08	Rehab Record Stage changed to *Handed to Listing*	Trigger listing workflow (create Listing Record or send notification to listing team – per Open Item O-WF002-05). Set Rehab Record Status = Closed. Set Rehab Record as read-only.	Immediate
A-RH-09	All Rehab Tasks linked to a Rehab Record change to Status = *Complete*	Notify Community Manager: "All rehab tasks complete – walkthrough can now be scheduled." Updates Rehab Record Stage to Walkthrough Scheduled only if manager confirms (prevents auto-skip of gate).	Immediate
A-RH-10	Rehab Record open > 30 days (Days In Rehab > 30) and Stage ≠ Approved or Handed to Listing	Send overdue alert email to Ops team with Rehab ID, current Stage, Days In Rehab, and Assigned To. Flag record with OVERDUE label in QB views.	Daily check
A-RH-11	Rehab Record open > 60 days (Days In Rehab > 60) and Stage ≠ Approved or Handed to Listing	Escalate to Austin (CEO) by email. Flag record as CRITICALLY OVERDUE in QB views. Include full stage history in alert. (See Open Item O-WF002-09 – confirm escalation path.)	Daily check

SECTION 08 Gate Rules

8 Hard Stops – No Bypass Permitted

Enforcement Principle: Gate rules are hard stops implemented as QB field-level validation or Pipeline checks. A gate that can be bypassed is not a gate. The Rehab Stage field must be locked to its current value until all conditions for the target stage are satisfied. Soft warnings are non-compliant.

Table 8-1 Gate Rules – WF002 Rehab

GATE ID	STAGE TRANSITION	CONDITION(S) – ALL MUST BE TRUE
G-RH-01	Rehab Identified → Scope Assessed	Scope Notes field is not blank. Community, Lot, and Asset are all linked (not null). RM Asset Record # and RM Unit # populated (warn if blank, not hard-block – per Open Item O-WF002-01).
G-RH-02	Scope Assessed → Work Assigned	Assigned To field is not blank.
G-RH-03	Work Assigned → Work In Progress	At least one Rehab Task record exists linked to this Rehab Record. At least one Rehab Task has Status = In Progress or Complete.
G-RH-04	Work In Progress → Walkthrough Scheduled	Walkthrough Scheduled Date is populated and is not a past date.
G-RH-05	Walkthrough Scheduled → Walkthrough Complete	At least one Rehab Walkthrough Record exists linked to this Rehab Record (confirmed via FastField webhook receipt and A-RH-05 execution).

G-RH-06	Walkthrough Complete → Approved	Walkthrough Status = "Approved as Ready to Market". Will not advance if Walkthrough Status = Needs Additional Items / Not Ready / Vendor Needs to Finish. Stage will route to Items To Resolve (Stage 7) via A-RH-07 instead.
G-RH-07	Items To Resolve → Walkthrough Scheduled	All Rehab Tasks linked to this Rehab Record have Status = Complete. No tasks with Status = Not Started / In Progress / Blocked. Enforces that re-inspection is not booked until all open items are resolved.
G-RH-08	Approved → Handed to Listing	Approved Date is populated. Asset Status = Available. Listing team confirmation received (method per Open Item O-WF002-05).

SECTION 09 Open Items

10 Open – All Assigned to Austin

All items below require a decision before the associated build step can be finalised. Items are not blocking the spec itself – they are blocking the implementation of the steps they reference. When resolved, the decision becomes binding for that step with no further change requests in scope without a document revision.

Table 9-1 Open Items Register – WF002 v1.0

ID	CATEGORY	DESCRIPTION	OWNER	STATUS
O-WF002-01	Trigger	Is WF002 always triggered automatically by a Move Out completion? Or can it also be triggered manually – e.g., for acquired homes, homes with existing damage identified during routine inspection? Recommend: support both auto and manual triggers; confirm whether Triggered By = Acquisition is in scope.	Austin	OPEN
O-WF002-02	Scope / Budget	Is there a cost or budget tracking component to Rehab? Should Rehab Records include fields for estimated cost, actual cost, and/or vendor invoice amounts? If yes, this adds fields to Table 4.1 (Rehab Records) and potentially a sub-table for line-item costs.	Austin	OPEN
O-WF002-03	Work Orders	Should Rehab Tasks (Table 4.2) be simple QB task records as currently specced, or is a formal Work Order document needed – one that can be sent to vendors via email from QB or accessed through a vendor portal? Formal work orders require additional design for the output document and vendor notification logic.	Austin	OPEN
O-WF002-04	Vendors	Is a Vendors table required in QB? (Vendor name, type, contact info, communities served.) A Vendors table enables vendor assignment via dropdown (rather than free-text), vendor-level reporting, and structured notification routing. Required if Work Orders (O-WF002-03) are implemented.	Austin	OPEN
O-WF002-05	Listing Handoff	When Rehab is Approved – does this auto-create a Listing Request record (in WF001 or a standalone listing workflow), or does the listing team manually initiate the listing process? The current spec has Automation A-RH-08 trigger the listing workflow, but the exact mechanism (auto-create vs. notify-and-wait) is TBD.	Austin	OPEN
O-WF002-06	Checklist Source	The 37-item Rehab Walkthrough Punchlist (7 sections) is derived from the JotForm audit provided. Confirm: Is this the complete, current checklist the team uses, or is there a more detailed version in use? Any additions or reordering affect the FastField form build and the QB Walkthrough Records table.	Austin	OPEN
O-WF002-07	Asset Status Values	"In Rehab" must be added as an Asset Status value in the Assets table before the cascading dropdown filter in Section 6 will work. Confirm the full set of Asset Status values to be supported: *In Rehab / Available / Listed / Occupied / Demo / Other* – or a different set?	Austin	OPEN

O-WF002-08	Lot Status for Rehab	A vacated lot currently carries Lot Status = Available. Should there be a separate Lot Status = In Rehab to distinguish actively rehabbing lots from genuinely available lots? Or is the rehab state tracked at the Asset level only (as currently specced in Section 6)? Decision affects lot-level dashboard filtering.	Austin	OPEN
O-WF002-09	Escalation Contact	Automation A-RH-11 escalates directly to Austin (CEO) after 60 days in rehab. Is this the correct escalation path, or should there be an intermediate escalation step – e.g., to a Regional Manager or VP of Operations – before CEO notification? Also confirm whether the 30-day (A-RH-10) and 60-day (A-RH-11) thresholds are appropriate, or whether different timeframes are preferred.	Austin	OPEN
O-WF002-10	Photo Documentation	The current FastField Rehab Walkthrough Punchlist spec does not include photo capture fields. Should photos be added? Options: (a) one photo field per section (7 photos total), (b) a photo capture triggered by any "No" answer (up to 37 prompts), or (c) a single "Additional Photos" field at the end of the form. Photos increase form build complexity but significantly improve deficiency documentation.	Austin	OPEN

SECTION 10 Spec Version History

Table 10-1 Document Version History

VERSION	DATE	AUTHOR	CHANGES
v1.0	08/18/26	Parakeet Build Team	Initial specification. 9 workflow stages (incl. 1 conditional loop), 3 QB tables (Rehab Records, Rehab Tasks, Walkthrough Records), 1 FastField form (37-item punchlist, 8 sections), 11 automations, 8 gate rules, 10 open items. Status: Draft for Review.
